ID	Task Name	Duration	Start	Finish	Predecessors
1	**Cambridge City Centre Cycle Parking Project**	**444.59 days**	**Wed 21/11/12**	**Thu 10/07/14**	
2					
3	**Officer Working Group**	**345 days**	**Wed 21/11/12**	**Wed 26/02/14**	
38	**Project Board Meeting**	**229.32 days**	**Tue 02/04/13**	**Fri 31/01/14**	
45					
46	**Project Initiation**	**21 days**	**Wed 21/11/12**	**Tue 18/12/12**	
47	Set-up PM Folder	1 day	Wed 21/11/12	Wed 21/11/12	
48	Background Research	2 wks	Wed 21/11/12	Wed 05/12/12	47
49	PM Structure	2 days	Wed 21/11/12	Fri 23/11/12	47
50	Produce Project Proposal	2 wks	Wed 05/12/12	Tue 18/12/12	49,48
51					
52	**Project Board Approval**	**5 days**	**Tue 18/12/12**	**Thu 27/12/12**	
53	Project Board Approval	1 wk	Tue 18/12/12	Thu 27/12/12	50
54					
55	**Preliminary Design**	**35 days**	**Tue 11/12/12**	**Wed 30/01/13**	
56	Identify potential location(s) for cycle park	2 wks	Tue 18/12/12	Thu 03/01/13	53SS
57	Identify potential locations for cycle racks	2 wks	Tue 18/12/12	Thu 03/01/13	56SS
58	Identify requests from Cllrs	2 wks	Tue 18/12/12	Thu 03/01/13	57SS
59	Identify requests from residents	2 wks	Tue 18/12/12	Thu 03/01/13	58SS
60	Identify requests from Cambridge Cycle Campaign	2 wks	Tue 18/12/12	Thu 03/01/13	59SS
61	Identify requests from Businesses	2 wks	Tue 18/12/12	Thu 03/01/13	60SS
62	Discussions with and buy-in agreements with facilities manager for cycle park space	2 wks	Thu 03/01/13	Wed 16/01/13	56
63	Project Board Review of proposed locations	1 wk	Wed 16/01/13	Wed 23/01/13	56,57,58,59,60,61,62
64	Set-up website for consultation	2 wks	Wed 16/01/13	Wed 30/01/13	63SS
65	Project Risk Log	35 days	Tue 11/12/12	Wed 30/01/13	56FF,57FF,58FF,59FF,60FF,61FF,62FF,63FF,64FF
66					
67	**Investigate Options for Secured Undercover Cycle Parking**	**176.22 days**	**Tue 18/12/12**	**Mon 12/08/13**	
68	Investigation of options for secured undercover cycle parking	7 mons	Tue 18/12/12	Wed 26/06/13	
69	Cost estimates for cycle park conversion	1 mon	Wed 26/06/13	Mon 22/07/13	68
70	Production of "Options Report" to be taken to ESC in October	4 mons	Mon 29/04/13	Mon 12/08/13	
71					
72	**ESC Approval - Scrutiny Report**	**22.7 days**	**Tue 12/02/13**	**Tue 12/03/13**	
73	Draft Scrutiny Report (Deadline: 12/02/2013)	0 days	Tue 12/02/13	Tue 12/02/13	56,57,58,59,60,61,62,63,64
74	Final Scrutiny Report (Deadline: 26/02/2013)	0 days	Tue 26/02/13	Tue 26/02/13	73
75	Env. Scrutiny Committee (ESC) Meeting 12/03/2013	0 days	Tue 12/03/13	Tue 12/03/13	
76	Update Risk Log	22.7 days	Tue 12/02/13	Tue 12/03/13	
77					
78	**Design - Detailed Design**	**50 days**	**Tue 12/03/13**	**Mon 20/05/13**	
79	New cycle rack locations	4 wks	Tue 12/03/13	Tue 09/04/13	75
80	BoQ estimates	4 wks	Tue 09/04/13	Fri 03/05/13	79
81	Project Board Review of Design	2 wks	Tue 07/05/13	Mon 20/05/13	79,80
82	Update Risk Log	50 days	Tue 12/03/13	Mon 20/05/13	
83					
84	**Area Committee Consultation**	**18 days**	**Tue 11/06/13**	**Wed 03/07/13**	
85	Final Report Deadline: 11/06/2013	0 days	Tue 11/06/13	Tue 11/06/13	79,80,81
86	West/Central Area Committee Meeting 20/06/2013	0 days	Thu 20/06/13	Thu 20/06/13	
87	Amend Design as required	2 wks	Thu 20/06/13	Wed 03/07/13	86
88	Update Risk Log	18 days	Tue 11/06/13	Wed 03/07/13	85FF,86FF,87FF
89					
90	**Consultation**	**50 days**	**Wed 03/07/13**	**Fri 06/09/13**	
91	Prepare consultation materials	2 wks	Wed 03/07/13	Tue 16/07/13	86,87
92	Public consultation/exhibition	6 wks	Tue 16/07/13	Fri 23/08/13	91
93	Resolve objections	2 wks	Fri 23/08/13	Fri 06/09/13	92
94	Asset Management Group (AMG)	2 wks	Mon 12/08/13	Fri 23/08/13	92FF
95	Update Risk Log	50 days	Wed 03/07/13	Fri 06/09/13	91FF,92FF,93FF,94FF
96					
97	**ESC Approval - Project Appraisal (On-Street) & Project Scrutiny (Off-street)**	**22 days**	**Tue 10/09/13**	**Tue 08/10/13**	
98	Draft Project Appraisal [on-street]; Draft Scrutiny Report [off-street] (Deadline: 10/09/2013)	0 days	Tue 10/09/13	Tue 10/09/13	91,92,93,94,70
99	Final Project Appraisal [on-street]; Final Scrutiny Report [off-street] (Deadline: 24/09/2013)	0 days	Tue 24/09/13	Tue 24/09/13	98
100	Env. Scrutiny Committee (ESC) Meeting 08/10/2013	0 days	Tue 08/10/13	Tue 08/10/13	
101	Update Risk Log	22 days	Tue 10/09/13	Tue 08/10/13	98FF,99FF,100FF
102					
103	**Design - Production of Information**	**70 days**	**Tue 08/10/13**	**Thu 09/01/14**	
104	Construction drawings	6 wks	Tue 08/10/13	Thu 14/11/13	100
105	Detailed costing	4 wks	Thu 14/11/13	Wed 11/12/13	104
106	Contract Specifications	4 wks	Wed 11/12/13	Thu 09/01/14	104,105
107	Update Risk Log	70 days	Tue 08/10/13	Thu 09/01/14	104FF,105FF,106FF
108					
109	**Procurement**	**20 days**	**Thu 09/01/14**	**Wed 05/02/14**	
110	Call off from Corporate Civils Framework Contract	4 wks	Thu 09/01/14	Wed 05/02/14	106
111	Update Risk Log	4 wks	Thu 09/01/14	Wed 05/02/14	110FF
112					
113	**Implementation**	**40 days**	**Wed 05/02/14**	**Fri 28/03/14**	
114	Mobilisation period	2 wks	Wed 05/02/14	Tue 18/02/14	110
115	Start work on site	1 day	Tue 18/02/14	Wed 19/02/14	114
116	Construction period	4 wks	Tue 18/02/14	Fri 14/03/14	115SS
117	Finish work on site	1 day	Fri 14/03/14	Fri 14/03/14	116FF
118	Snagging	2 wks	Mon 17/03/14	Fri 28/03/14	117
119	Update Risk Log	40 days	Wed 05/02/14	Fri 28/03/14	114FF,115FF,116FF,117FF,118FF
120					
121	**Post Project Review**	**35 days**	**Tue 18/02/14**	**Thu 03/04/14**	
122	Quality Review	6 wks	Tue 18/02/14	Fri 28/03/14	115FF,116FF,117FF,118FF
123	Project closure report	1 wk	Fri 28/03/14	Thu 03/04/14	117,118,122
124	Lessons learnt report	1 wk	Fri 28/03/14	Thu 03/04/14	123SS
125					
126	**Secured Undercover Cycle Parking Option**	**205.68 days**	**Tue 08/10/13**	**Thu 10/07/14**	
127	Detailed Design	3 mons	Tue 08/10/13	Tue 24/12/13	100
128	Consultation and Report Prep	10 days	Tue 24/12/13	Thu 09/01/14	127
129	West/Central Area Committee Meeting 09/01/2014	0 days	Thu 09/01/14	Thu 09/01/14	
130	Consultation	6 wks	Thu 09/01/14	Mon 17/02/14	129
131	Project Appraisal - ESC Meeting 11/03/2014	0 days	Tue 11/03/14	Tue 11/03/14	
132	Construction Drawings	4 wks	Tue 11/03/14	Fri 04/04/14	131
133	Procurement	4 wks	Fri 04/04/14	Fri 02/05/14	132
134	Implementation	2 mons	Tue 06/05/14	Thu 26/06/14	133
135	Post Porject Review	2 wks	Fri 27/06/14	Thu 10/07/14	134

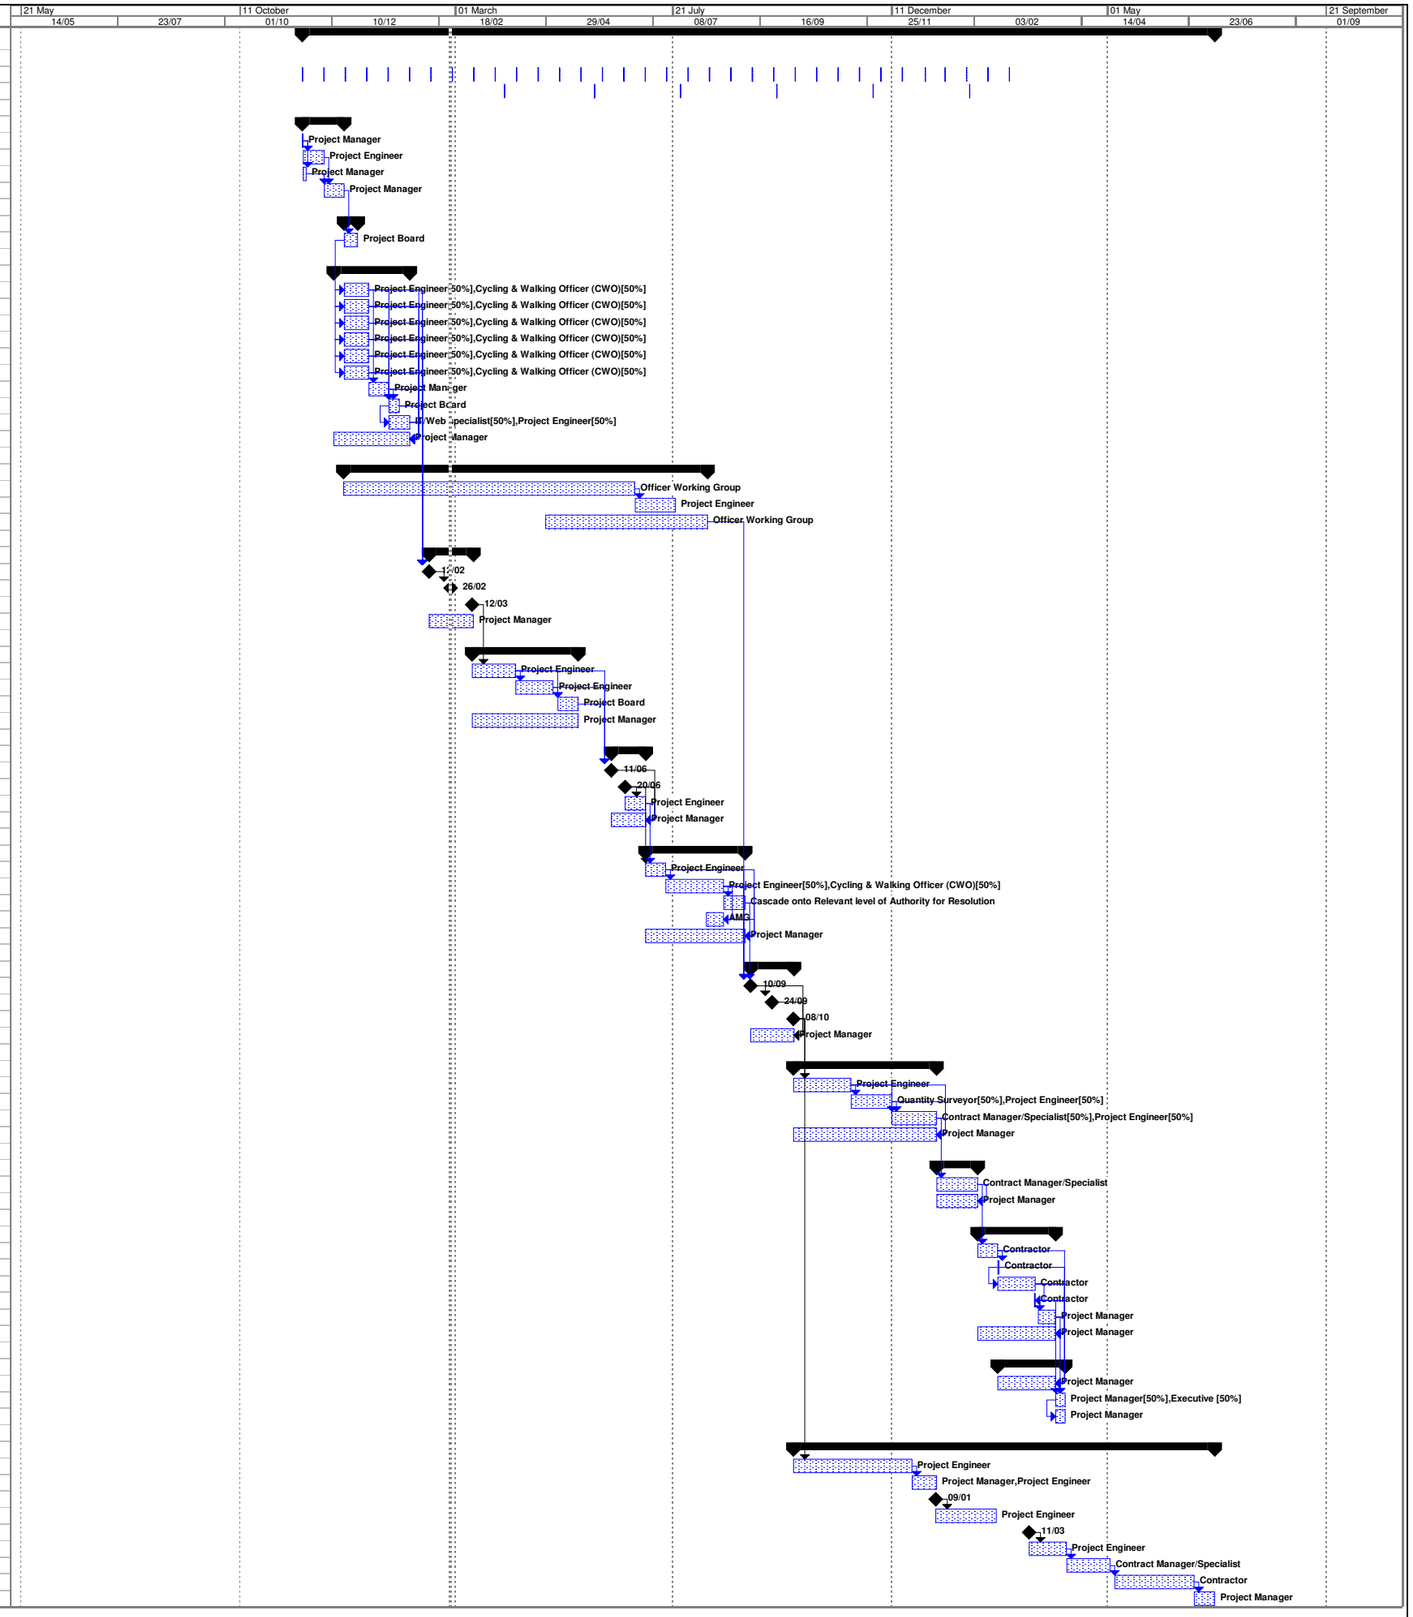

CCC Cycle Parking Project Programm
Date: Mon 25/02/13

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
