ID	Task Name	Duration	Start	Finish	% Complete
1	**CAMBRIDGE 20MPH PROJECT**	**899 days**	**Mon 22/10/12**	**Mon 02/05/16**	**78%**
2					
3	**Project Initiation/Approval**	**160 days**	**Mon 22/10/12**	**Tue 11/06/13**	**100%**
23					
24	**Phase 1**	**473 days**	**Tue 22/01/13**	**Mon 24/11/14**	**100%**
32					
67	**PHASE 2 - EAST AREA**	**532 days**	**Tue 08/10/13**	**Wed 11/11/15**	**77%**
68	**Phase 2 Engagement/Detailed Design**	**362 days**	**Tue 08/10/13**	**Wed 18/03/15**	**100%**
75					
76	**Phase 2 Consultation**	**138 days**	**Thu 28/11/13**	**Wed 18/06/14**	**100%**
93					
94	**Phase 2 Traffic Orders + Victoria Road**	**150 days**	**Mon 01/09/14**	**Wed 08/04/15**	**0%**
101					
102	**Phase 2 Implementation + Victoria Road**	**135 days**	**Mon 06/10/14**	**Wed 22/04/15**	**0%**
110					
111	**Phase 2 Review**	**25 days**	**Thu 08/10/15**	**Wed 11/11/15**	**0%**
114					
115	**PHASE 3 (FINAL) WEST/CENTRAL & SOUTH AREA'S**	**423 days**	**Mon 08/09/14**	**Mon 02/05/16**	**0%**
116	**Phase 3 Design**	**107 days**	**Mon 29/09/14**	**Fri 06/03/15**	**0%**
117	Commission/Undertake/Analyse ATCs	6 wks	Mon 29/09/14	Fri 07/11/14	0%
118	Review Consultation Feedback	2 wks	Mon 12/01/15	Fri 23/01/15	0%
119	Detailed Design	1 mon	Mon 26/01/15	Fri 20/02/15	0%
120	Detailed Cost Estimate	2 wks	Mon 23/02/15	Fri 06/03/15	0%
121					
122	**Phase 3 Consultation/Approvals**	**128 days**	**Mon 08/09/14**	**Tue 17/03/15**	**0%**
123	Write Reports for South & W/C Area Committee's (Inform Consultation)	2 wks	Mon 08/09/14	Fri 19/09/14	0%
124	Submit Draft Report to SAC & WCAC	0 days	Fri 19/09/14	Fri 19/09/14	0%
125	Update reports as required	1 wk	Mon 22/09/14	Fri 26/09/14	0%
126	**SAC**	0 days	Mon 13/10/14	Mon 13/10/14	0%
127	**WCAC**	0 days	Wed 29/10/14	Wed 29/10/14	0%
128	Finalise Consultation Material	2 wks	Wed 22/10/14	Tue 04/11/14	0%
129	Public Consultation Period inc. drop-ins etc.	8 wks	Wed 05/11/14	Fri 09/01/15	0%
130	Assess & Summarise Consultation Results	2 wks	Mon 12/01/15	Fri 23/01/15	0%
131	Write & Submit Final Report to SAC & WCAC (recommendations)	1 wk	Mon 19/01/15	Fri 23/01/15	0%
132	**SAC**	0 days	Mon 02/02/15	Mon 02/02/15	0%
133	**WCAC**	0 days	Thu 05/03/15	Thu 05/03/15	0%
134	Write ESC Report - approval to implement final phase	1 wk	Mon 26/01/15	Fri 30/01/15	0%
135	Submit Draft ESC Report	0 days	Fri 30/01/15	Fri 30/01/15	0%
136	Submit Final ESC Report	0 days	Fri 06/03/15	Fri 06/03/15	0%
137	**ESC Approval to Implement**	0 days	Tue 17/03/15	Tue 17/03/15	0%
138					
139	**Phase 3 Traffic Orders**	**95 days**	**Tue 17/03/15**	**Mon 27/07/15**	**0%**
140	Advertise Traffic Orders	2 mons	Tue 17/03/15	Mon 11/05/15	0%
141	Prepare objections report to CJAC	2 wks	Tue 12/05/15	Mon 25/05/15	0%
142	CJAC determine objections (June date to be confirmed)	5 wks	Tue 26/05/15	Mon 29/06/15	0%
143	Make Orders to coincide with final sign installation	1 mon	Tue 30/06/15	Mon 27/07/15	0%
144					
145	**Phase 3 Implementation**	**125 days**	**Tue 21/04/15**	**Mon 12/10/15**	**0%**
146	Finalise Detailed Design	1 mon	Tue 21/04/15	Mon 18/05/15	0%
147	Produce Works Package	2 wks	Tue 19/05/15	Mon 01/06/15	0%
148	Procure Contractor	1 mon	Tue 02/06/15	Mon 29/06/15	0%
149	Implementation	3 mons	Tue 30/06/15	Mon 21/09/15	0%
150	Monitor Implementation	3 mons	Tue 30/06/15	Mon 21/09/15	0%
151	Snagging	3 wks	Tue 22/09/15	Mon 12/10/15	0%
152	Sign Off	0 days	Mon 12/10/15	Mon 12/10/15	0%
153					
154	**Phase 3**	**25 days**	**Tue 29/03/16**	**Mon 02/05/16**	**0%**
155	Undertake ATCs to monitor against KPIs	3 wks	Tue 29/03/16	Mon 18/04/16	0%
156	Review Results	2 wks	Tue 19/04/16	Mon 02/05/16	0%

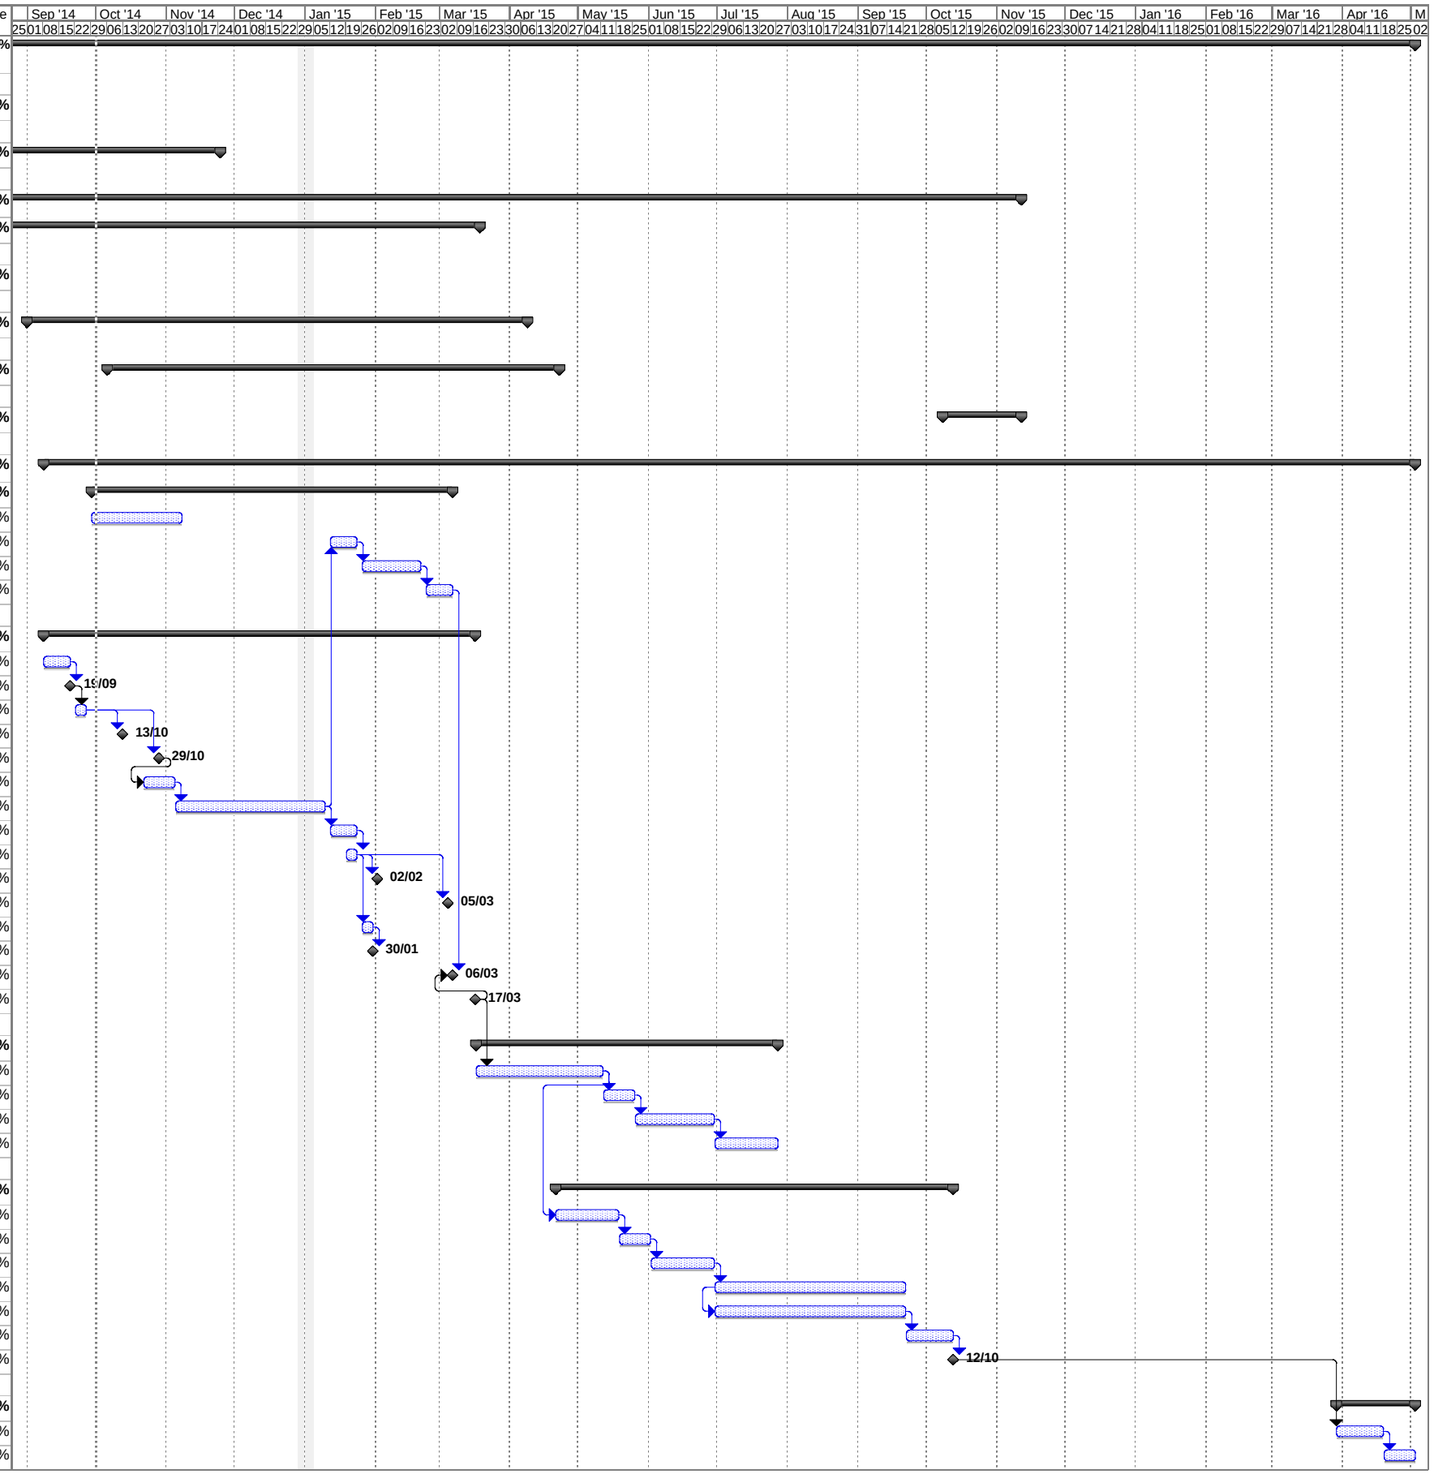

Project: 20mph Project Programme Re
Date: Wed 01/10/14

Task | Progress | Summary | External Tasks | Split
Split | Milestone | Project Summary | External MileTask
